

FOLLOW-UP 1 OF 3

Nine-capability coverage: current, future and vendors

Management view as of the 30 September 2026 milestone (date to confirm)

Capability	Velora by 30 Sep	Velora beyond Sep	Protiviti claim	MeshX scope
C1 Enterprise data query	Covered — 6 SAP queries live	Expand via SAP BDC/BTP + Foundry	Full — SAP + SharePoint/OneLake	Foundation MCP; 3–5 questions
C2 Recommendations	Covered — daily KPI scan	Broader signals and skills	Full — Foundry scheduled skill	Not covered
C3 Evaluation engine	In progress — close and evidence	Deeper criteria/data models	Full — Foundry evaluation skill	Not covered
C4 Briefing & synthesis	Covered — inbox briefs/digests	More sources and automation	Full — cited Outlook/Teams briefs	Not covered
C5 Agent creation	Gated — governance + lifecycle	Full governed self-service	Full — create/edit/pause/retire	Not covered
C6 Institutional memory	Covered — documents/transcripts	Broader corpus and retention	Full — AI Search/RAG	Not covered
C7 Meeting intelligence	Covered — Graph + action flows	Broader channels/automation	Full — Graph/manual upload	Not covered
C8 Peer benchmarking	Planned — one approved source	Multi-source benchmarking	Full — one-source minimum	Not covered
C9 Decision traceability	Partial — Dataverse live; export/Purview	Dual audit + full governance	Full — Dataverse + CSV evidence	Data lineage/audit portion only

VELORA: 5 COMPLETE • 2 ACTIVE/PARTIAL • 2 GATED/PLANNED

PROTIVITI: 9 CLAIMED — NOT YET DELIVERED

MESHX: C1 + DATA-LAYER C9 ONLY

Key point: Protiviti is broader; MeshX is deeper only in governed data/lineage. Velora can reach capability parity without rebuilding the current SAP path.

FOLLOW-UP 2 OF 3

What Velora must complete to cover Protiviti’s claims

Internal ownership is available; the remaining need is protected capacity, evidence and management decisions

Close the four remaining capability items

- C3 — complete structured evaluation and evidence.
- C5 — confirm “without IT” governance; prove create/edit/pause/retire.
- C8 — demonstrate benchmarking against one approved source.
- C9 — complete evidence schema and CSV export; use Dataverse if Purview is delayed.

Retest the five capabilities already covered

- C1 — six permission-trimmed SAP queries.
 - C2 — scheduled KPI recommendations.
 - C4 — executive briefing and synthesis.
 - C6 — searchable documents/transcripts.
 - C7 — meeting intelligence and action flows.
- Output: signed tests, screenshots, logs and business acceptance.

Add Protiviti-equivalent delivery controls

- Requirements traceability matrix • formal SIT/integration/security/negative-path tests • UAT scripts and CEO/proxy booking • capability-level ADAA evidence • controlled release/rollback • runbooks, monitoring and full internal hypercare.

ACCOUNTABILITY

Owner	Role	Accountability
Bala	Developer Architect + Project Manager	Architecture, traceability, delivery plan, RAID/defects, documentation and coordination
Abdullah + Infrastructure team	Infrastructure and access	Non-Prod/Prod support, connectivity, environments, production readiness and access
SAP leads	Lakshmi • Abdelaziz • Kamalesh • Xavier • Rajesh • Kamal	System, integration, permission, security and negative-path testing
David • Shiva • Lakshmi	Business/UAT	UAT scripts, CEO/proxy sessions, expected results and business sign-off
Abdelaziz + Bala	Evidence and operations	ADAA evidence pack, runbooks, monitoring, incident ownership and escalation


Management position: Phase 1 can be covered internally. Additional resources do not replace the owners above—they create the capacity to fast-track C3/C5/C8/C9 and complete testing/evidence without weakening go-live support.

FOLLOW-UP 3 OF 3

Delivery path: September completion and beyond-timeline scale

Keep Phase 1 stable; introduce SAP BDC, Azure AI Foundry/Azure Foundry and SAP DevOps as a governed next phase

DELIVERY TIMELINE

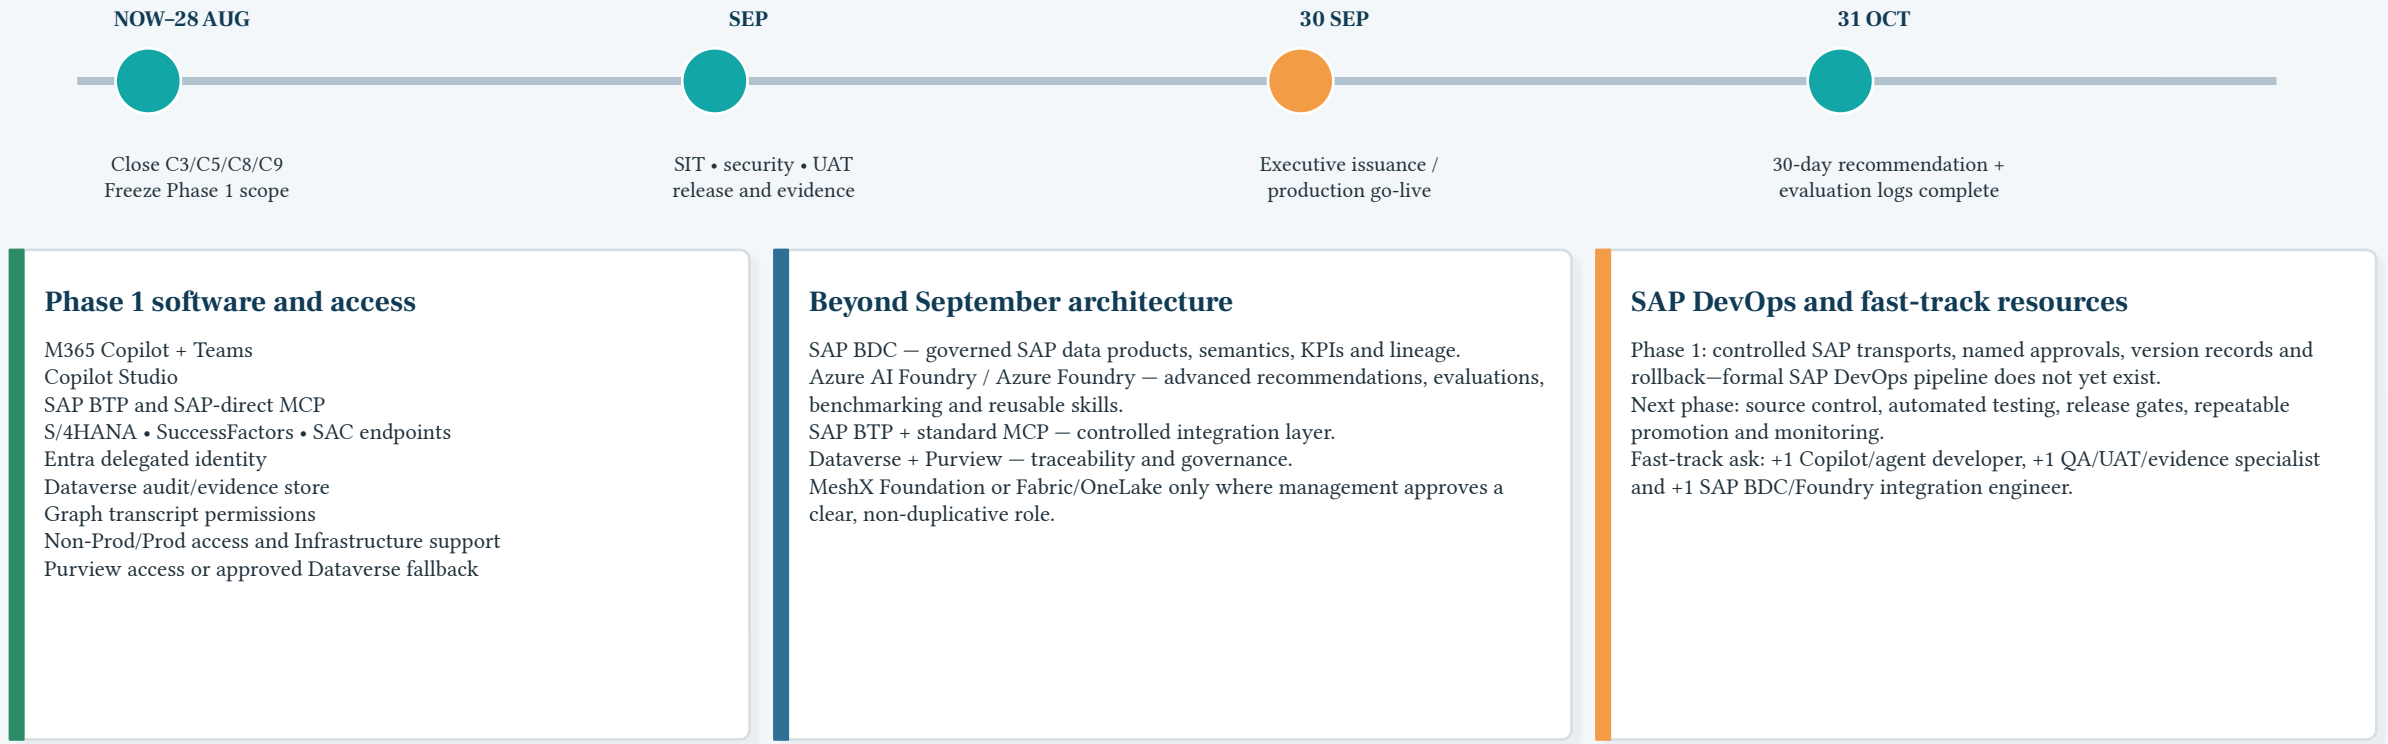

DECISION REQUIRED

Protect the existing internal owners through go-live and approve a small surge team to fast-track the remaining capabilities. Treat SAP BDC + Azure AI Foundry/Azure Foundry + SAP DevOps as a separately governed next-phase roadmap—not a September re-platforming exercise.
